


Riverside Program Update - 07/01/16

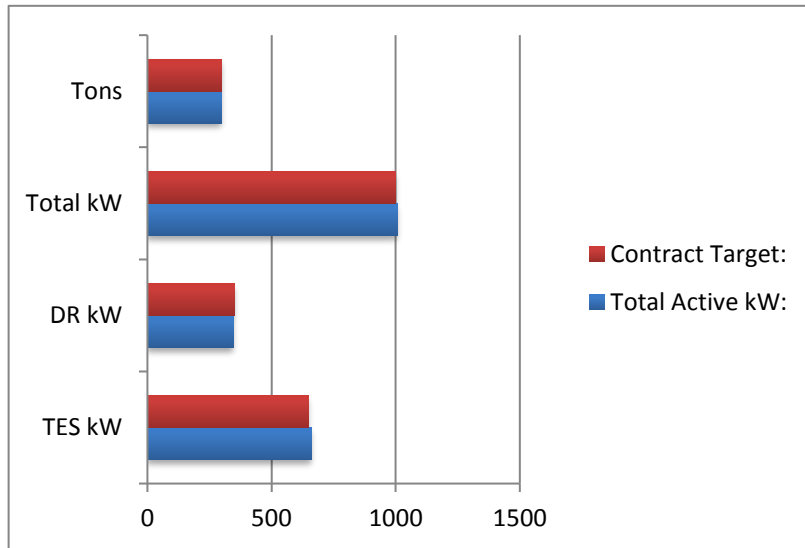

Total Active kW & Tons by Stage				
Site Stat	TES kW	DR kW	Total kW	Tons
Signed:	76.4	76.4	152.8	80
Commissioned:	585.4	270.6	856	217.5
Total Active kW:	661.8	347	1008.8	297.5
Contract Target:	650	350	1000	300
% of Target:	102%	99%	101%	99%

Program % Breakdown			
	TES	DR	Total
Target %:	65%	35%	100%
Current Program %:	66%	34%	100%

	Values									
Sites	HVAC Units Targeted	Ice Bears	Ice Bear - Tons	DR - Tons	HVAC - # Replaced	HVAC - Tons Rep	HVAC Rep Savings - kWh	Ice Bear - kW	DR - kW	Total - kW
City	41	17	173.25	103.75	15	98	53,251	311.6	182	493.6
Commissioned	41	17	173.25	103.75	15	98	53,251	311.6	182	493.6
Airport	9	3	29	18	6	35	18,866	55.5	34.6	90.1
Arlington Library	6	3	30	16		0	-	48.6	25.3	73.9
Bordwell Park	4	2	22.25	12.25	1	12.5	6,738	37.8	21.6	59.4
Bryant Park	4	1	12	12		0	-	19.2	19.2	38.4
Building Service & Fleet (Corporate Yard)	4	1	9	10	2	9	2,590	14.2	13.8	28
Janet Goeske Center	8	4	41	17	4	24	15,624	78.3	32.3	110.6
Magnolia Police Department	3	1	7.5	6	1	7.5	4,043	14.5	11.2	25.7
Villegas Park	3	2	22.5	12.5	1	10	5,390	43.5	24	67.5
Commercial	46	19	187.5	92.5	26	199.5	110,821	350.2	165	515.2
Construction	8	4	40	40	8	80	43,124	76.4	76.4	152.8
Cal Baptist University, Van Dyne Gym	8	4	40	40	8	80	43,124	76.4	76.4	152.8
Commissioned	38	15	147.5	52.5	18	119.5	67,697	273.8	88.6	362.4
BMW Motorcycles of Riverside	4	1	10	9	2	10	5,390	19.2	15.9	35.1

	Values									
Sites	HVAC Units Targeted	Ice Bears	Ice Bear - Tons	DR - Tons	HVAC - # Replaced	HVAC - Tons Rep	HVAC Rep Savings - kWh	Ice Bear - kW	DR - kW	Total - kW
Bud's Tire	4	1	10	0	2	10	6,050	19.9	0	19.9
Cal Baptist University, Post	4	1	10.5	8.5	2	6.5	4,362	15.1	15	30.1
Cal Baptist University, Simmons Hall	2	4	40	0	2	40	21,560	78.4	0	78.4
Gar Labs	4	2	19	0		0	-	30	0	30
Hertz Corp	3	1	10	10	1	10	5,390	19.5	13.5	33
Riverside Auto Holdings Inc-Singh	4	1	9	7	2	9	5,299	17.2	11	28.2
Fritts Ford (Annex)	3	1	10	3	2	10	6,710	20.6	6.1	26.7
Fritts Ford (Main Building)	10	3	29	15	5	24	12,936	53.9	27.1	81
Grand Total	87	36	360.75	196.25	41	297.5	164,072	661.8	347	1008.8
